


Executive Summary

■■■■■ ■■■■■■

Project Code	128
Tower	128
Last Update	30/6/2026
Report Date	2026-09-04 11:59

Metric	Value
Total Flats	125
Total System Points	180
Average Flats Progress	47.3%
Average Systems Progress	21.7%

Flats Progress Details

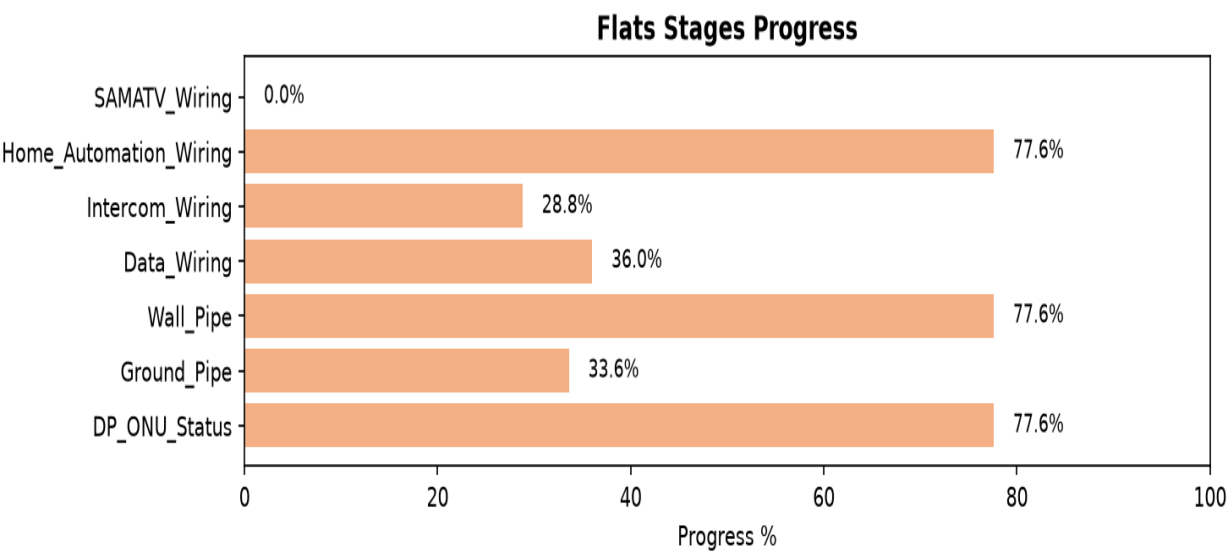

Stage	Done	Pending	Progress %
DP ONU Status	97	28	77.6%
Ground Pipe	42	83	33.6%
Wall Pipe	97	28	77.6%
Data Wiring	45	80	36.0%
Intercom Wiring	36	89	28.8%
Home Automation Wiring	97	28	77.6%
SAMATV Wiring	0	125	0.0%


Sample Flat Details (First 15)

Flat #	Type	Floor	Done Stages	Status
101	2BHK	1	6/7	In Progress
102	2BHK	1	5/7	In Progress
103	1BHK	1	5/7	In Progress
104	1BHK	1	6/7	In Progress
105	2BHK	1	6/7	In Progress
106	1BHK	1	5/7	In Progress
107	2BHK	1	6/7	In Progress
108	studio	1	6/7	In Progress
109	studio	1	6/7	In Progress
110	studio	1	6/7	In Progress

111	studio	1	6/7	In Progress
112	1BHK	1	6/7	In Progress
113	studio	1	5/7	In Progress
201	2BHK	2	6/7	In Progress
202	2BHK	2	5/7	In Progress


Systems Progress Details

System: Access Control

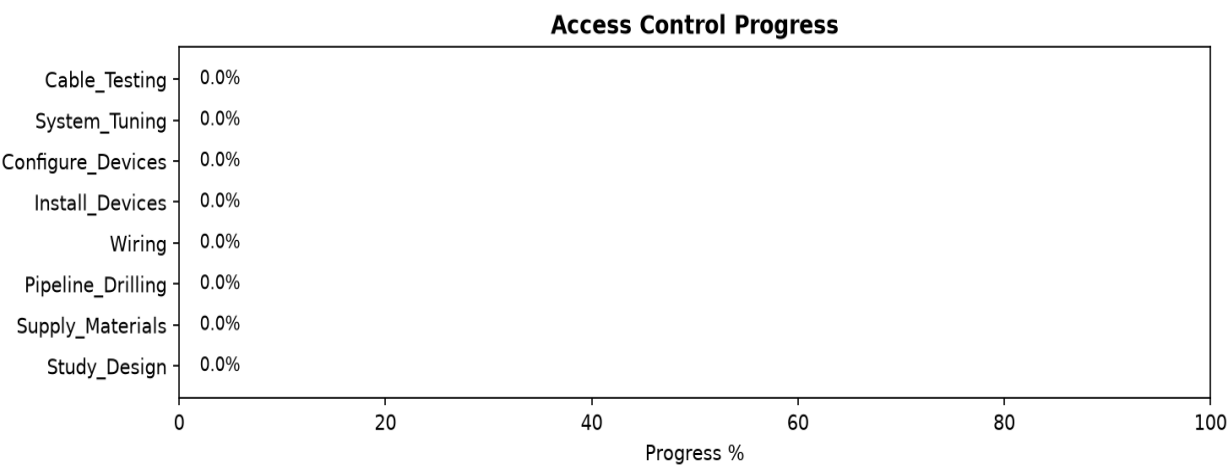


Stage	Done	Pending	Progress %
Study Design	0	12	0.0%
Supply Materials	0	12	0.0%
Pipeline Drilling	0	12	0.0%
Wiring	0	12	0.0%
Install Devices	0	12	0.0%
Configure Devices	0	12	0.0%
System Tuning	0	12	0.0%
Cable Testing	0	12	0.0%

System: CCTV

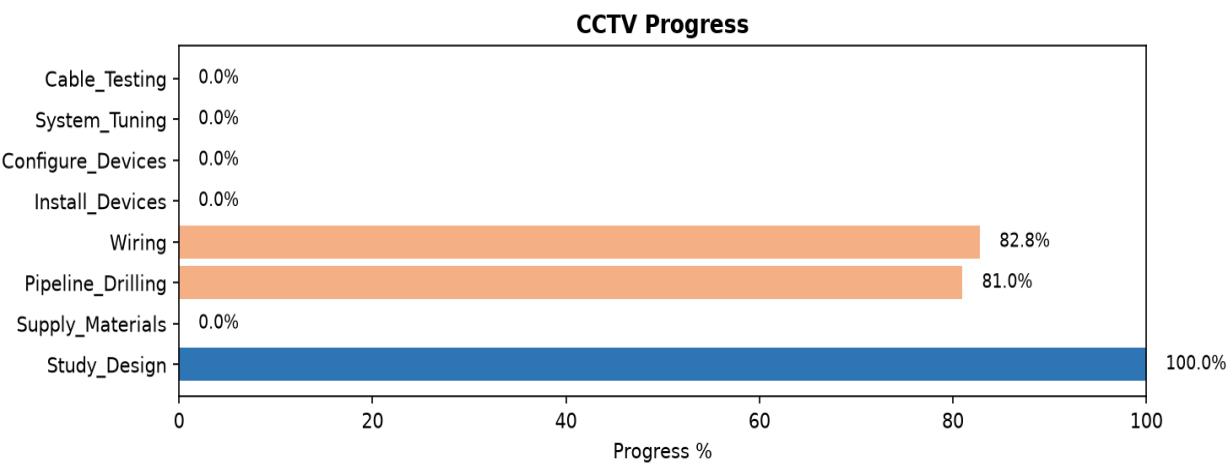


Stage	Done	Pending	Progress %
Study Design	58	0	100.0%
Supply Materials	0	58	0.0%
Pipeline Drilling	47	11	81.0%
Wiring	48	10	82.8%
Install Devices	0	58	0.0%
Configure Devices	0	58	0.0%
System Tuning	0	58	0.0%
Cable Testing	0	58	0.0%

System: Fiber Optic

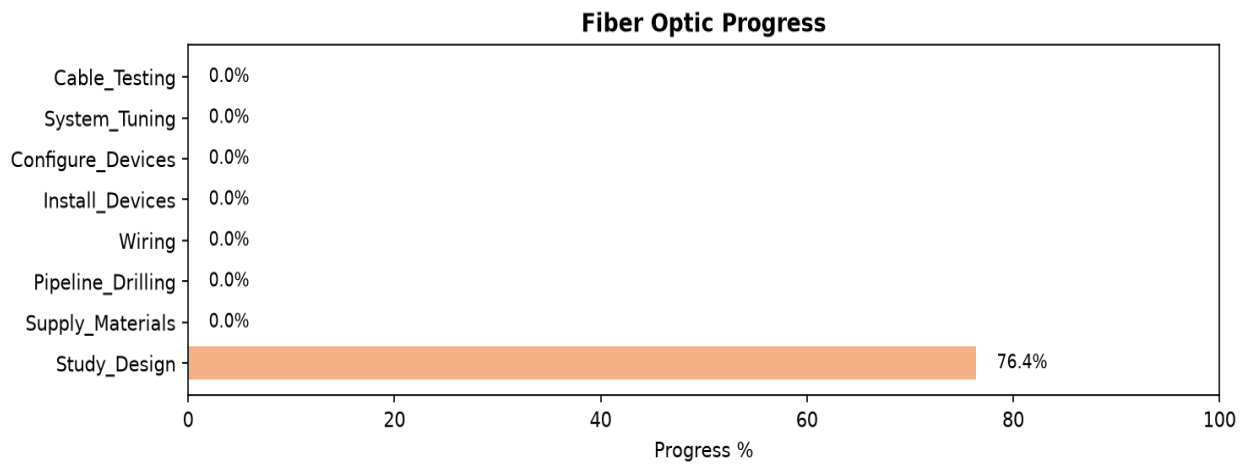


Stage	Done	Pending	Progress %
Study Design	42	13	76.4%
Supply Materials	0	55	0.0%
Pipeline Drilling	0	55	0.0%
Wiring	0	55	0.0%
Install Devices	0	55	0.0%
Configure Devices	0	55	0.0%
System Tuning	0	55	0.0%
Cable Testing	0	55	0.0%

System: Inter Come

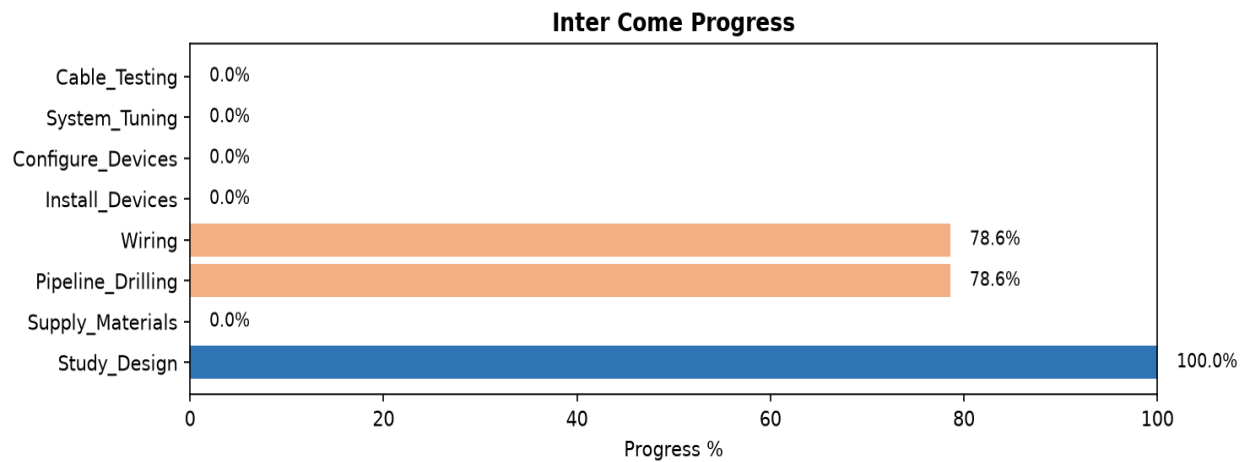

Stage	Done	Pending	Progress %
Study Design	14	0	100.0%
Supply Materials	0	14	0.0%
Pipeline Drilling	11	3	78.6%
Wiring	11	3	78.6%
Install Devices	0	14	0.0%
Configure Devices	0	14	0.0%
System Tuning	0	14	0.0%
Cable Testing	0	14	0.0%

System: intercom

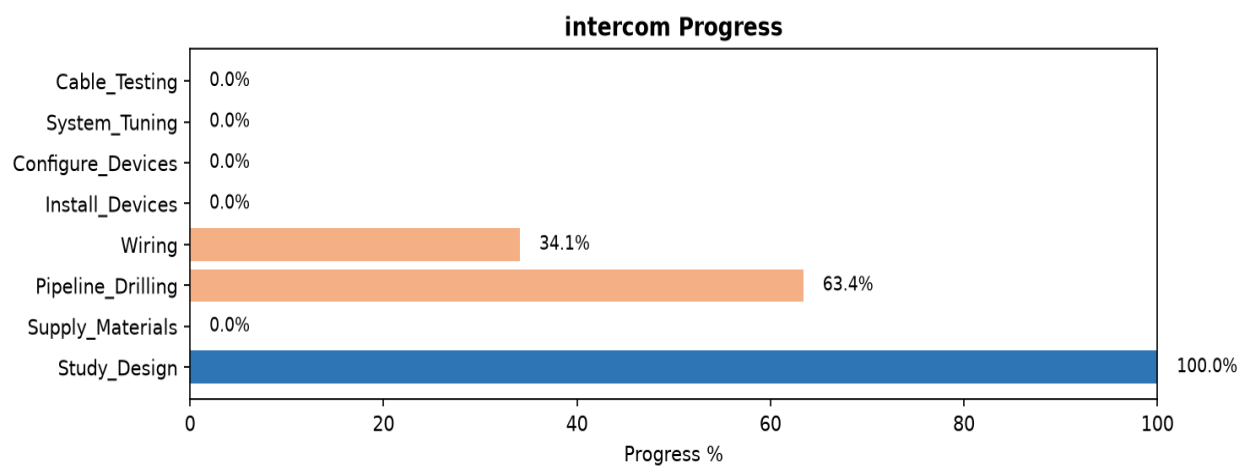

Stage	Done	Pending	Progress %
Study Design	41	0	100.0%
Supply Materials	0	41	0.0%
Pipeline Drilling	26	15	63.4%
Wiring	14	27	34.1%

Install Devices	0	41	0.0%
Configure Devices	0	41	0.0%
System Tuning	0	41	0.0%
Cable Testing	0	41	0.0%
